



OREGON

Debris Management  
Task Force

# Wildfire Debris & Hazard Tree Removal Update

HOUSE SPECIAL COMMITTEE ON WILDFIRE RECOVERY



APRIL 5, 2021




## Weekly topline points | from the week of March 29-April 2

- **+175 cleared sites completed this week for a total of 1,064 statewide** (out of 2,856 total home sites).
- Hazard tree marking and removal steadily progressing: **61,969 trees marked and 21,443 removed** of the more than 290,000 estimated statewide. We continue to hear a mix of strong reactions to the noticeable changes in the landscape left by the 2020 wildfires.
- **We expect to complete debris removal work in the Echo Mountain fire area in the coming month. Asking for any remaining Right-of-Entries to be submitted by April 15<sup>th</sup>.** To ensure that all fire-impacted property owners have the option to participate before crews complete work on current ROEs, we're asking remaining property owners to submit a Right-of-Entry form by April 15<sup>th</sup>.
- **Planning for and protecting cultural resources and archeological sites in southern Oregon continues as a top priority for hazard tree removal operations.** We are taking the necessary time to pause and plan as we work with the tribal community, contractors, and others to ensure identified cultural sites are respected and protected.




# Data dashboard by fire and interactive status map <https://bit.ly/3bMyqBl>

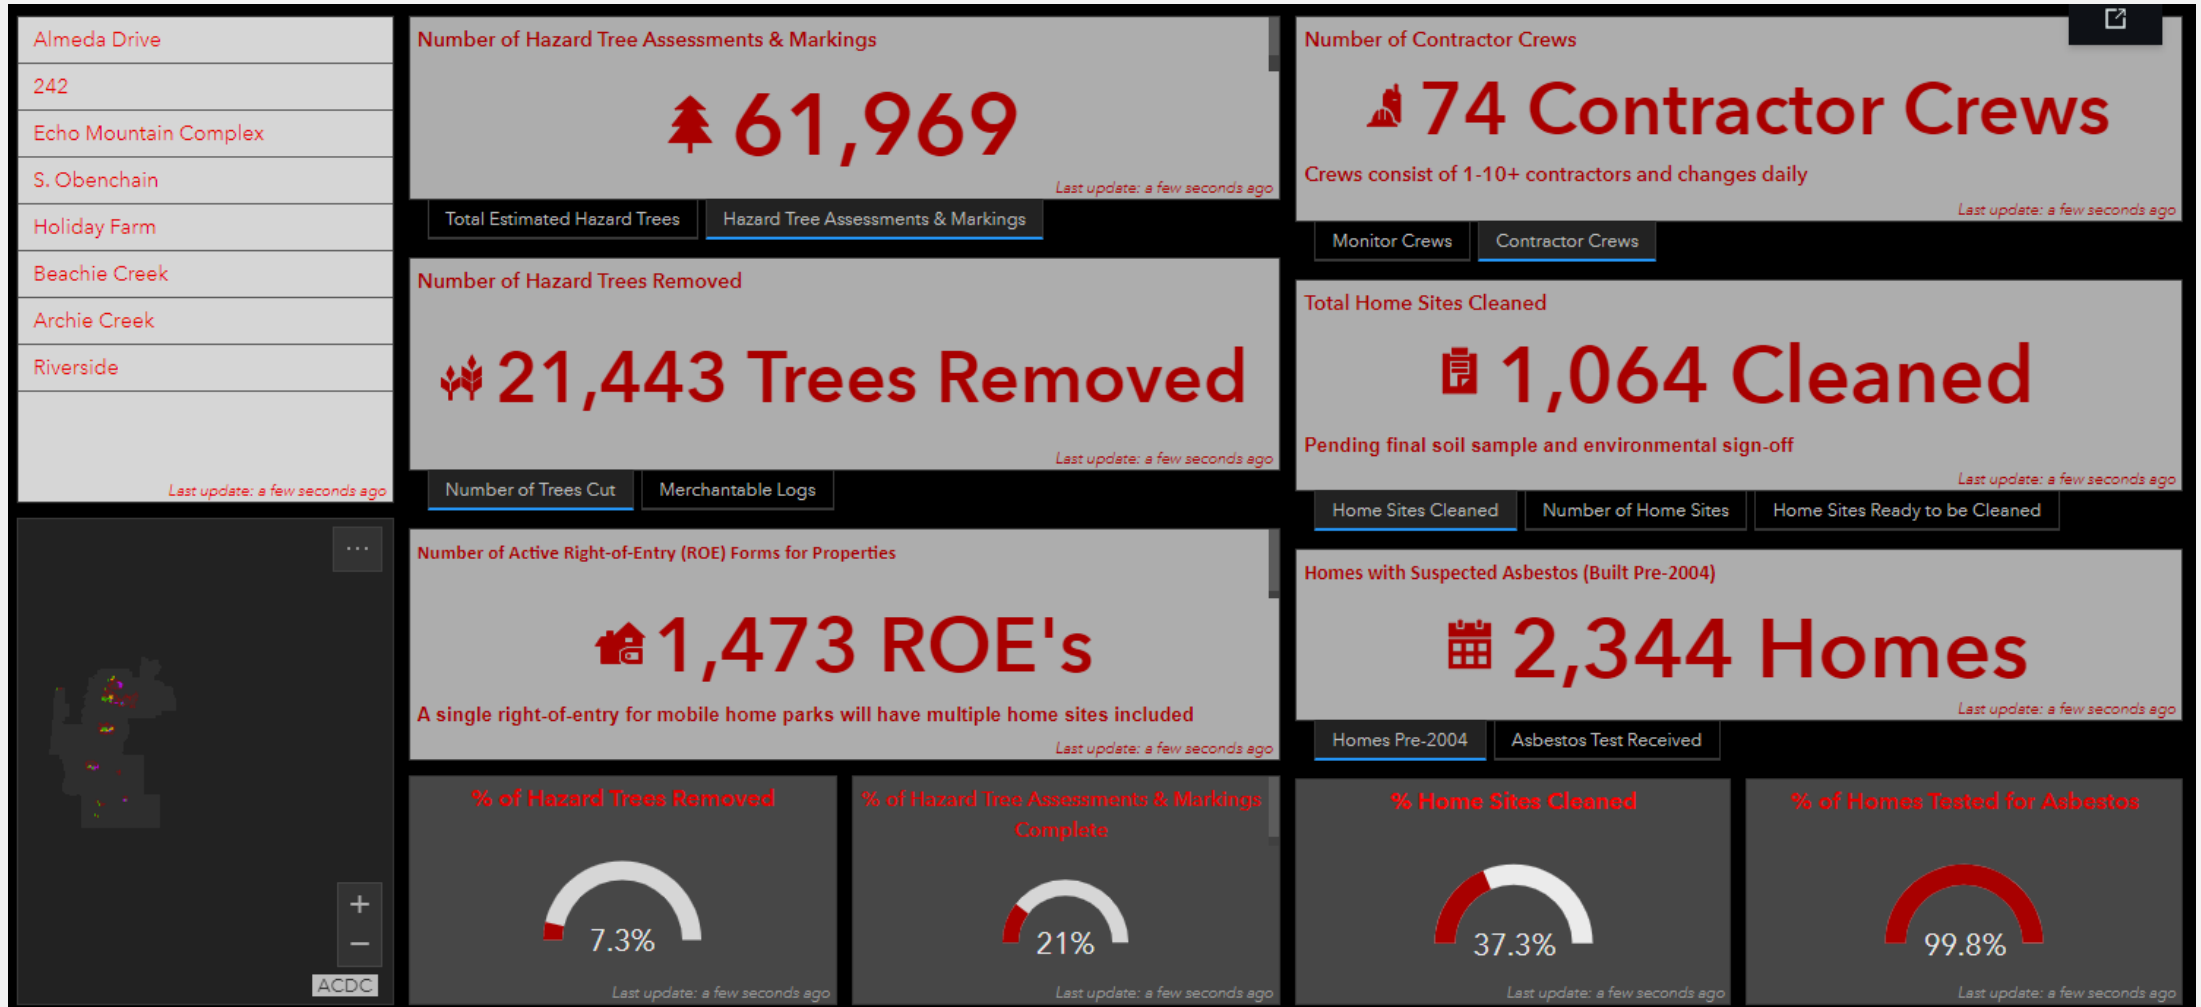

\*Data captured on Friday, April 2

# Hazard Tree Removal and Private Property Debris Removal look ahead: northern Oregon

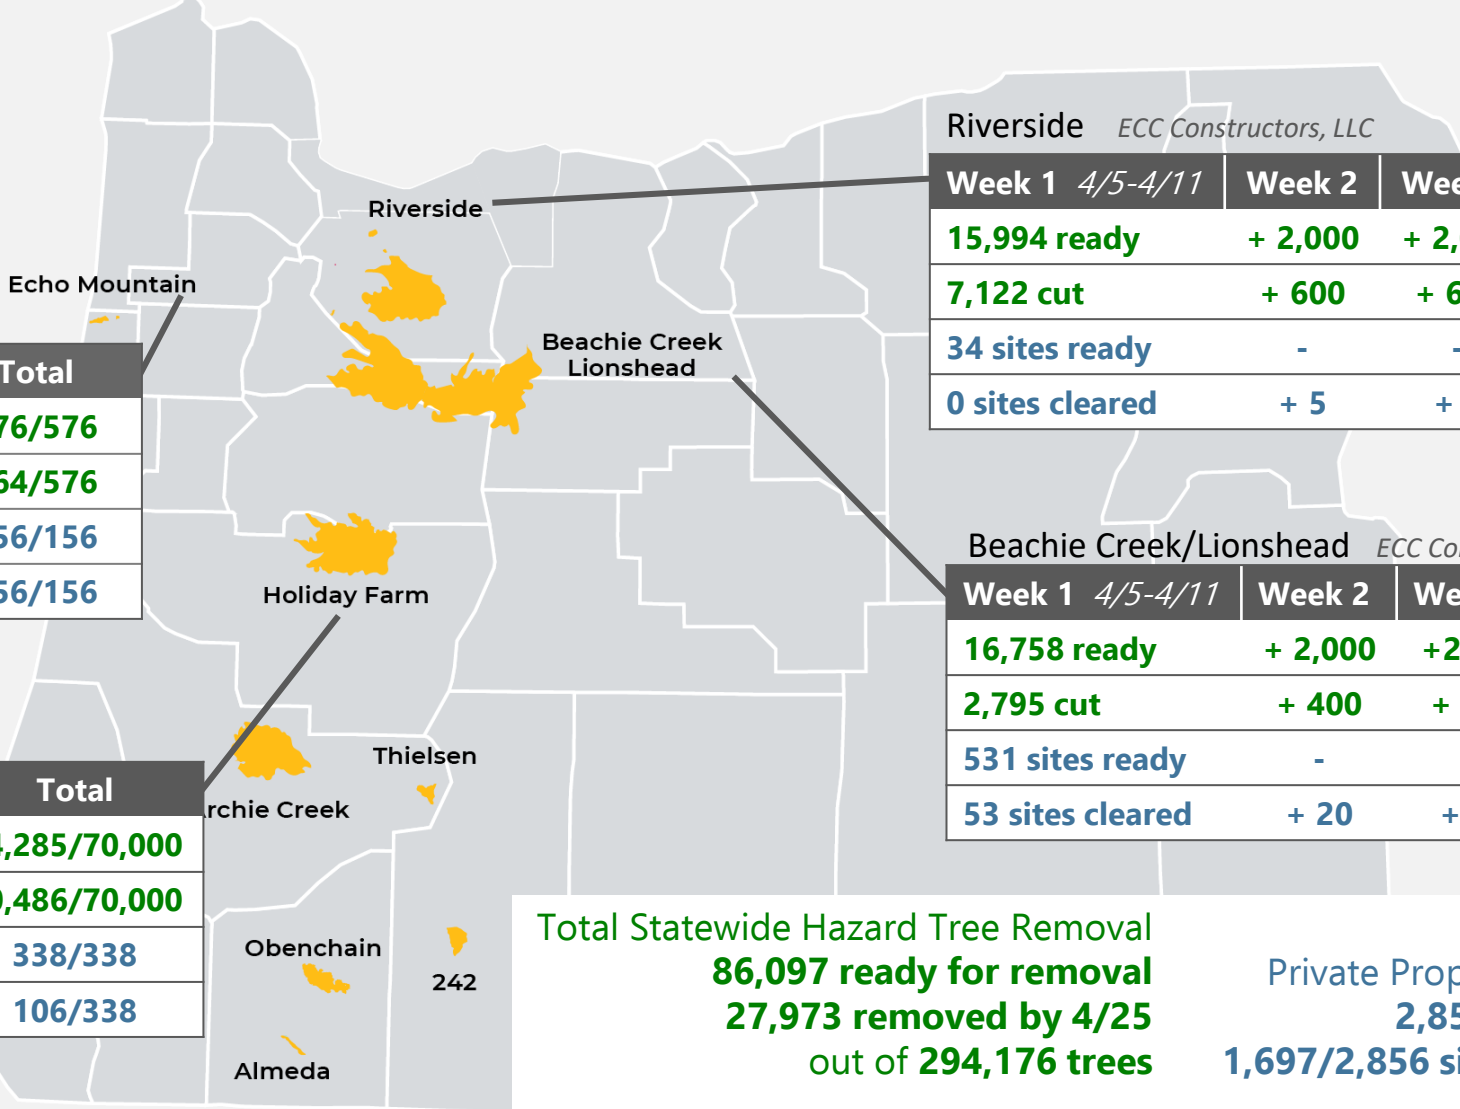

Echo Mountain *K&E Excavating, Inc.*

Week 1 4/5-4/11	Week 2	Week 3	Total
<b>576 ready</b>	-	-	<b>576/576</b>
<b>244 cut</b>	+ 10	+ 10	<b>264/576</b>
<b>156 sites ready</b>	-	-	<b>156/156</b>
<b>98 sites cleared</b>	+ 30	+ 28	<b>156/156</b>

Holiday Farm *Suulutaaq, AshBritt Environmental*

Week 1 4/5-4/11	Week 2	Week 3	Total
<b>20,285 ready</b>	+ 2,000	+ 2,000	<b>24,285/70,000</b>
<b>9,486 cut</b>	+ 500	+ 500	<b>10,486/70,000</b>
<b>338 sites ready</b>	-	-	<b>338/338</b>
<b>66 sites cleared</b>	+ 20	+ 20	<b>106/338</b>

Riverside *ECC Constructors, LLC*

Week 1 4/5-4/11	Week 2	Week 3	Total
<b>15,994 ready</b>	+ 2,000	+ 2,000	<b>19,994/113,000</b>
<b>7,122 cut</b>	+ 600	+ 600	<b>8,322/113,000</b>
<b>34 sites ready</b>	-	-	<b>34/34</b>
<b>0 sites cleared</b>	+ 5	+ 5	<b>10/34</b>

Beachie Creek/Lionshead *ECC Constructors, LLC*

Week 1 4/5-4/11	Week 2	Week 3	Total
<b>16,758 ready</b>	+ 2,000	+ 2,000	<b>20,758/57,000</b>
<b>2,795 cut</b>	+ 400	+ 400	<b>3,995/57,000</b>
<b>531 sites ready</b>	-	-	<b>531/531</b>
<b>53 sites cleared</b>	+ 20	+ 20	<b>93/531</b>

Total Statewide Hazard Tree Removal  
**86,097 ready for removal**  
**27,973 removed by 4/25**  
 out of **294,176 trees**

Total Statewide  
 Private Property Debris Removal  
**2,856/2,856 sites ready**  
**1,697/2,856 sites cleared by 4/25**

# Hazard Tree Removal and Private Property Debris Removal look ahead: southern Oregon

Archie Creek *Ceres Environmental, K&E Excavating, Inc.*

Week 1 4/5-4/11	Week 2	Week 3	Total
<b>11,514 ready</b>	<b>+ 2,000</b>	<b>+ 2,000</b>	<b>15,514/49,000</b>
<b>3,345 cut</b>	<b>+ 600</b>	<b>+ 600</b>	<b>4,545/49,000</b>
<b>77 sites ready</b>	-	-	<b>77/77</b>
<b>21 sites cleared</b>	<b>+ 10</b>	<b>+ 10</b>	<b>41/77</b>

Obenchain *To be assigned shortly*

Week 1 4/5-4/11	Week 2	Week 3	Total
-	-	-	-
-	-	-	-
<b>17 sites ready</b>	-	-	<b>17/17</b>
<b>0 sites cleared</b>	<b>+ 5</b>	<b>+ 5</b>	<b>10/17</b>

Almeda *Ashbritt Environmental*


Week 1 4/5-4/11	Week 2	Week 3	Total
<b>2,750 ready</b>	-	-	<b>2,750/2,750</b>
<b>0 cut</b>	-	<b>+ 100</b>	<b>100/2,750</b>
<b>1,691 sites ready</b>	-	-	<b>1,691/1,691</b>
<b>1,031 sites cleared</b>	<b>+ 120</b>	<b>+ 120</b>	<b>1,271/1,691</b>

Thielsen *Ceres Environmental*

Week 1 4/5-4/11	Week 2	Week 3	Total
-	-	-	-
-	-	-	-
-	-	-	-
-	-	-	-

242 *Ceres Environmental, K&E Excavating, Inc.*

Week 1 4/5-4/11	Week 2	Week 3	Total
<b>2,220 ready</b>	-	-	<b>2,220/2,220</b>
<b>0 cut</b>	<b>0</b>	<b>+ 100</b>	<b>100/2,220</b>
<b>12 sites ready</b>	-	-	<b>12/12</b>
<b>0 sites cleared</b>	<b>+ 5</b>	<b>+ 5</b>	<b>10/12</b>

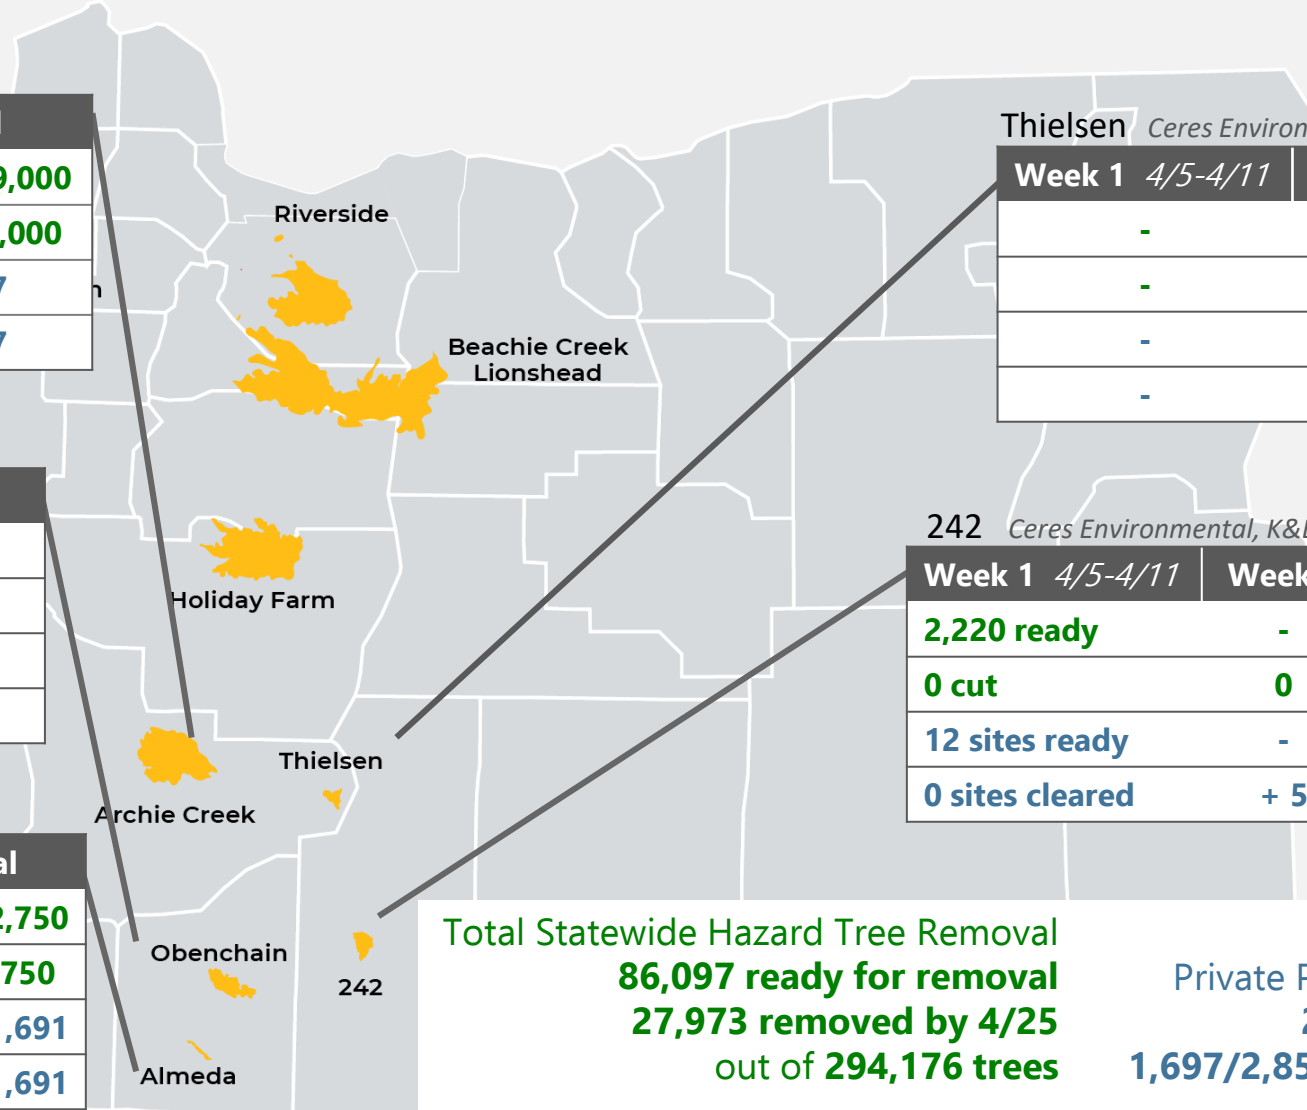

Total Statewide Hazard Tree Removal  
**86,097 ready for removal**  
**27,973 removed by 4/25**  
 out of **294,176 trees**

Total Statewide Private Property Debris Removal  
**2,856/2,856 sites ready**  
**1,697/2,856 sites cleared by 4/25**

# Track status with us



[Youtube.com/OregonDOT](https://www.youtube.com/OregonDOT)



[Twitter.com/OregonOEM](https://twitter.com/OregonOEM)



[Flickr.com/oregondot](https://www.flickr.com/oregondot)

Webpage, interactive status map, dashboard  
[wildfire.oregon.gov/cleanup](https://wildfire.oregon.gov/cleanup)

Debris news page  
[www.DebrisCleanupNews.com](http://www.DebrisCleanupNews.com)



[odot.wildfire@odot.state.or.us](mailto:odot.wildfire@odot.state.or.us)



**Hotline: 503-934-1700**
