



OREGON

Debris Management
Task Force

Wildfire Debris & Hazard Tree Removal Update

HOUSE SPECIAL COMMITTEE ON WILDFIRE RECOVERY



MAY 7, 2021




DEAN O'DONNELL
PRESIDENT, DETROIT LAKE RECREATIONAL
AREA BUSINESS ASSOCIATION



Weekly topline points | from the week of May 3-7

- **We have officially completed the halfway point for participating home sites cleared. +152 cleared sites completed this week for a total of 1,663 statewide** (out of 2,824 total home sites).
- **75,955 fire-damaged trees marked and 31,484 removed** of the more than 140,000 estimated statewide. Trees are marked through a series of reviews and quality control measures.
- **Helping support tourism and economic development priorities in Detroit.** Visit www.debriscleanupnews.com to watch the video and see how our work is supporting rebuilding and Detroit's next chapter.
- **Next steps in fire recovery efforts for fire-damaged trees:** independent arborist/forester, internal review, and ensuring an adaptive operation as part of emergency response work.
- **The hotline 503-934-1700** is always available to help answer questions and coordinate concerns.

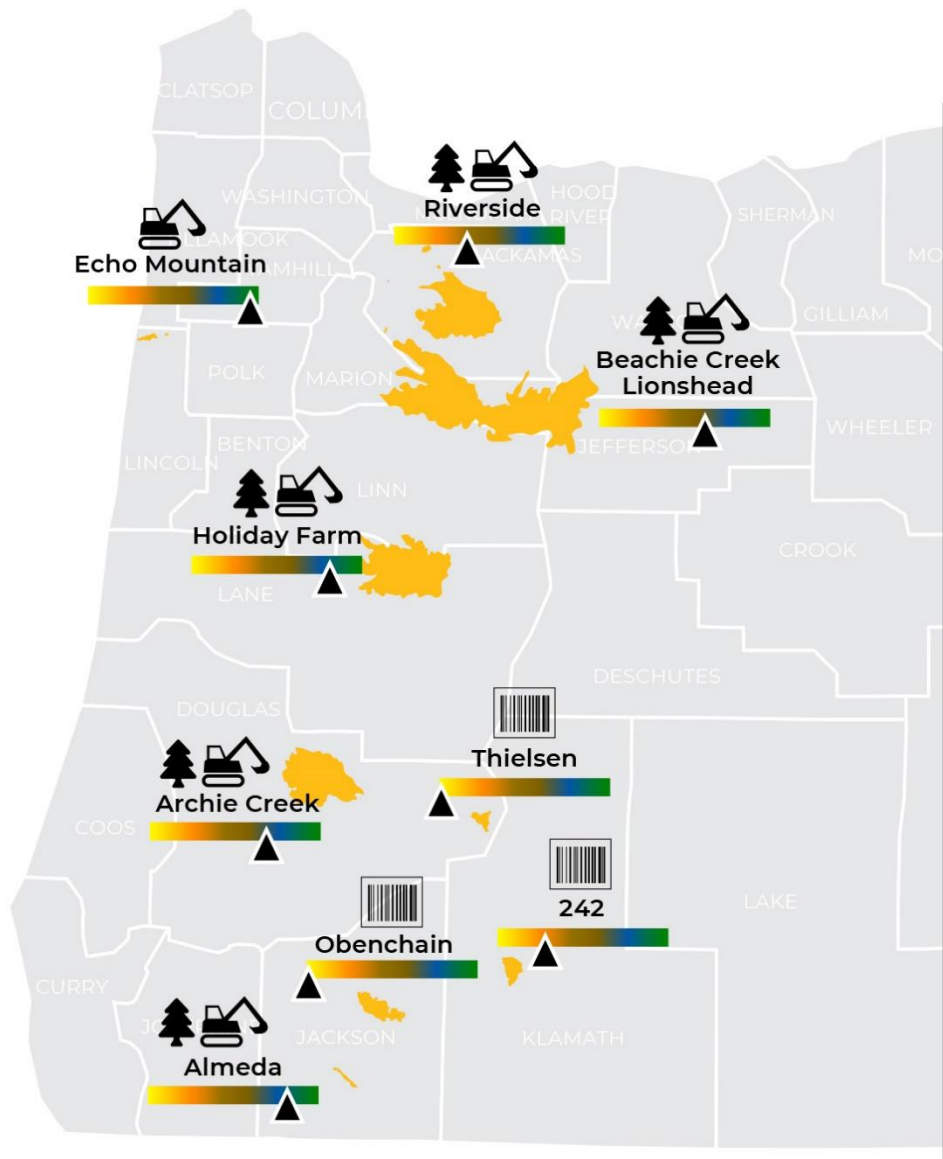


1,663 home sites
 cleared
 throughout
 Oregon

1,417 properties
 and **2,824 home sites**
 currently
 participating in
 the Step 2
 cleanup
 process 

75,955 trees
 marked and
 ready to
 be cut 

31,484 hazard
 trees removed 


BY THE NUMBERS

As of Thursday 5/06/21

- **1,417 properties and 2,824 home sites participating** through complete Right of Entry forms (this number fluctuates).
- **Number of crews working:** 104 contractor crews, 63 monitoring crews currently working.
- **Data dashboard** by fire and interactive status map: <https://bit.ly/3bMyqBl>



Hazard Tree Removal and Private Property Debris Removal look ahead: northern Oregon

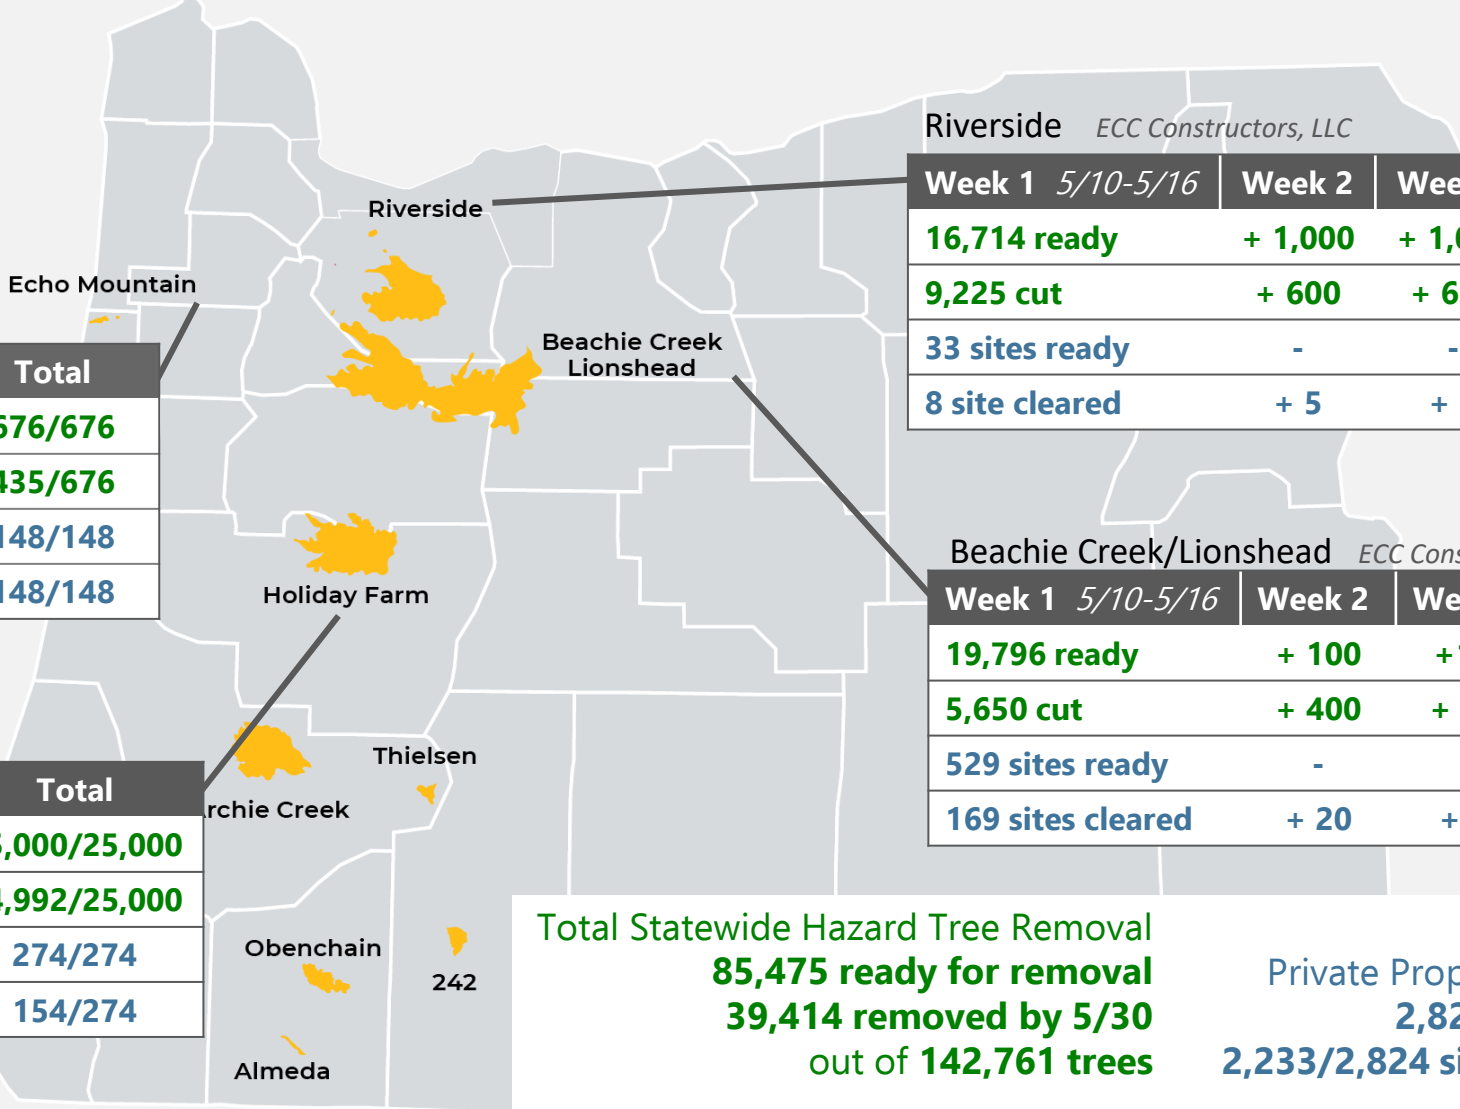

Echo Mountain *K&E Excavating, Inc.*

Week 1 5/10-5/16	Week 2	Week 3	Total
674 ready	-	+ 2	676/676
415 cut	+ 10	+ 10	435/676
148 sites ready	-	-	148/148
148 sites cleared	-	-	148/148

Holiday Farm *Suulutaaq, AshBritt Environmental*

Week 1 5/10-5/16	Week 2	Week 3	Total
23,457 ready	+ 1,000	+ 543	25,000/25,000
13,992 cut	+ 500	+ 500	14,992/25,000
274 sites ready	-	-	274/274
114 sites cleared	+ 20	+ 20	154/274

Riverside *ECC Constructors, LLC*

Week 1 5/10-5/16	Week 2	Week 3	Total
16,714 ready	+ 1,000	+ 1,000	18,714/74,334
9,225 cut	+ 600	+ 600	10,425/74,334
33 sites ready	-	-	33/33
8 site cleared	+ 5	+ 5	18/33

Beachie Creek/Lionshead *ECC Constructors, LLC*

Week 1 5/10-5/16	Week 2	Week 3	Total
19,796 ready	+ 100	+ 104	20,000/20,000
5,650 cut	+ 400	+ 400	6,450/20,000
529 sites ready	-	-	529/529
169 sites cleared	+ 20	+ 20	209/529

Total Statewide Hazard Tree Removal
85,475 ready for removal
39,414 removed by 5/30
 out of **142,761 trees**

Total Statewide Private Property Debris Removal
2,824/2,824 sites ready
2,233/2,824 sites cleared by 5/30

Hazard Tree Removal and Private Property Debris Removal look ahead: southern Oregon

Archie Creek *Ceres Environmental, K&E Excavating, Inc.*

Week 1 5/10-5/16	Week 2	Week 3	Total
10,150 ready	+ 1,000	+ 1,000	12,150/13,415
3,615 cut	+ 600	+ 600	4,815/13,415
78 sites ready	-	-	78/78
38 sites cleared	+ 10	+ 10	58/78

Obenchain *To be assigned shortly*

Week 1 5/10-5/16	Week 2	Week 3	Total
-	-	-	-
-	-	-	-
17 sites ready	-	-	17/17
0 sites cleared	+ 5	+ 5	10/17

Alameda *Ashbritt Environmental*


Week 1 5/10-5/16	Week 2	Week 3	Total
3,403 ready	+ 50	+ 61	3,514/3,632
1,197 cut	+ 500	+ 500	2,197/3,632
1,733 sites ready	-	-	1,733/1,733
1,386 sites cleared	+ 120	+ 120	1,626/1,733

Thielsen *Ceres Environmental*

Week 1 5/10-5/16	Week 2	Week 3	Total
-	-	-	-
-	-	-	-
-	-	-	-
-	-	-	-

242 *Ceres Environmental, K&E Excavating, Inc.*

Week 1 5/10-5/16	Week 2	Week 3	Total
5,421 ready	-	-	5,421/5,704
0 cut	0	+ 100	100/5,704
12 sites ready	-	-	12/12
0 sites cleared	+ 5	+ 5	10/12

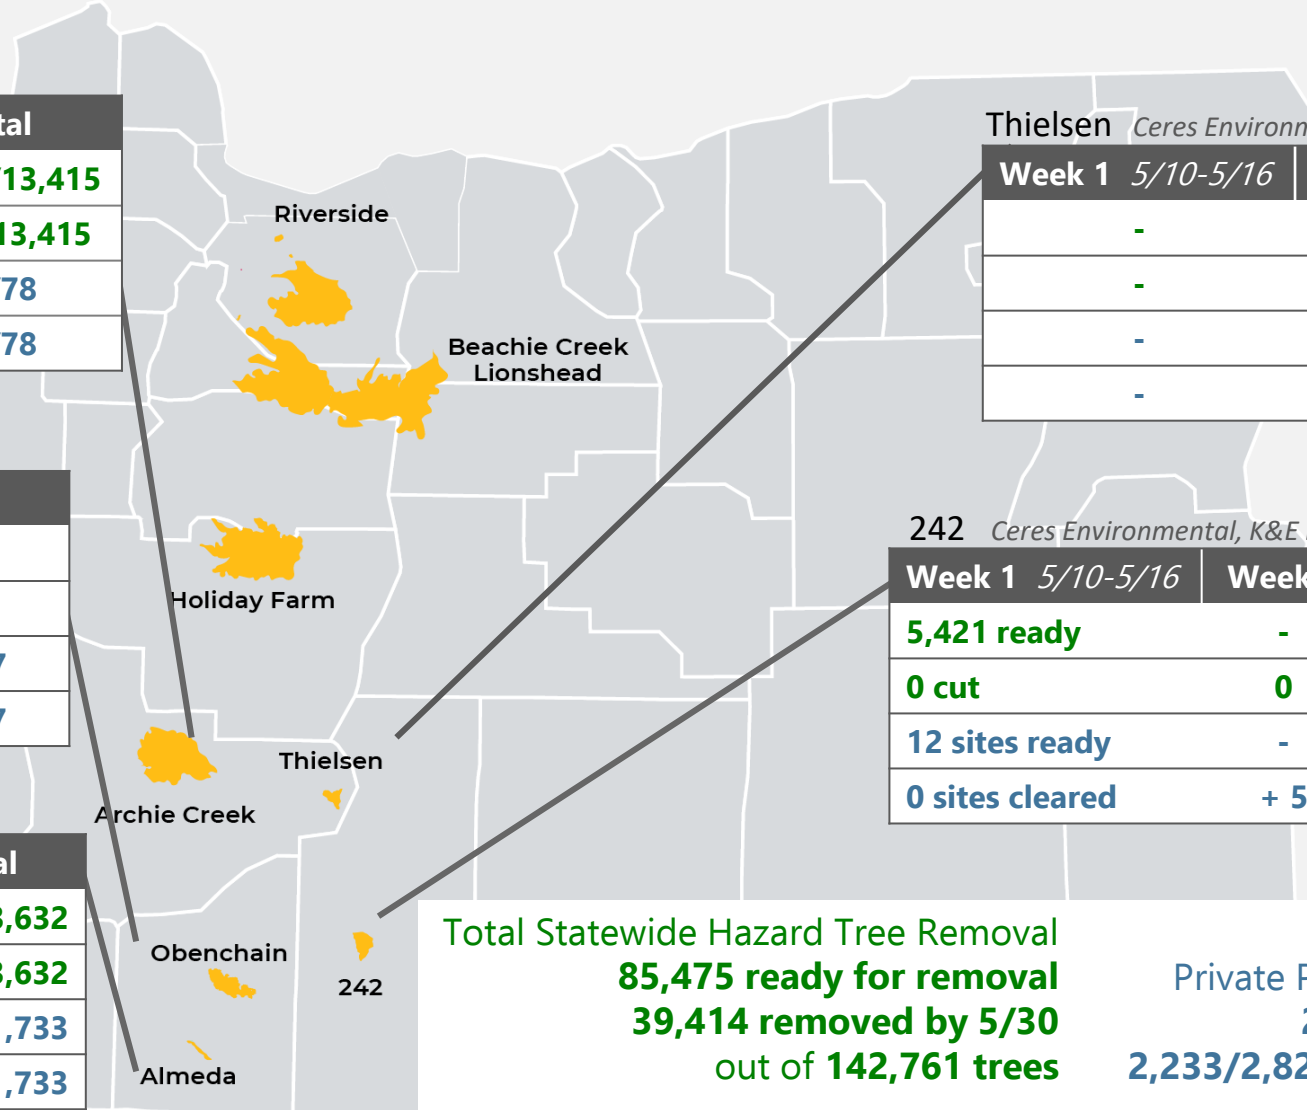

Total Statewide Hazard Tree Removal
85,475 ready for removal
39,414 removed by 5/30
 out of **142,761 trees**

Total Statewide Private Property Debris Removal
2,824/2,824 sites ready
2,233/2,824 sites cleared by 5/30

Track status with us



[Youtube.com/OregonDOT](https://www.youtube.com/OregonDOT)



[Twitter.com/OregonOEM](https://twitter.com/OregonOEM)



[Flickr.com/oregondot](https://www.flickr.com/oregondot)

Webpage, interactive status map, dashboard
wildfire.oregon.gov/cleanup

Debris news page
www.DebrisCleanupNews.com



odot.wildfire@odot.state.or.us



Hotline: 503-934-1700
