



OREGON

Debris Management  
Task Force

# Wildfire Debris & Hazard Tree Removal Update

HOUSE SPECIAL COMMITTEE ON WILDFIRE RECOVERY




MARCH 15, 2021





## Weekly summary points | from the week of March 8-12

- Continued dry weather and accelerated pace added 140 cleared sites this week **for a total of 472 completed home sites statewide** (out of 2,986 total). More than 120 monitoring and contract crews are in the field working for Oregon.
- Hazard tree work actively continues: **42,007 trees marked and 10,201 removed** of the more than 290,000 estimated statewide.
- **Direct outreach calls to property owners continues to be appreciated and a valuable offline connection.** We want to ensure everyone has the information they need throughout this process.
- **We helped McKenzie School District return to school today** after Task Force crews cleared nearly 800 trees in less than a week.
- **Challenges to note:** very busy highway corridors, high winds and falling rocks in Riverside Fire area, ensuring everyone has the opportunity to opt-in while crews are in their area, property access and steep terrain challenges

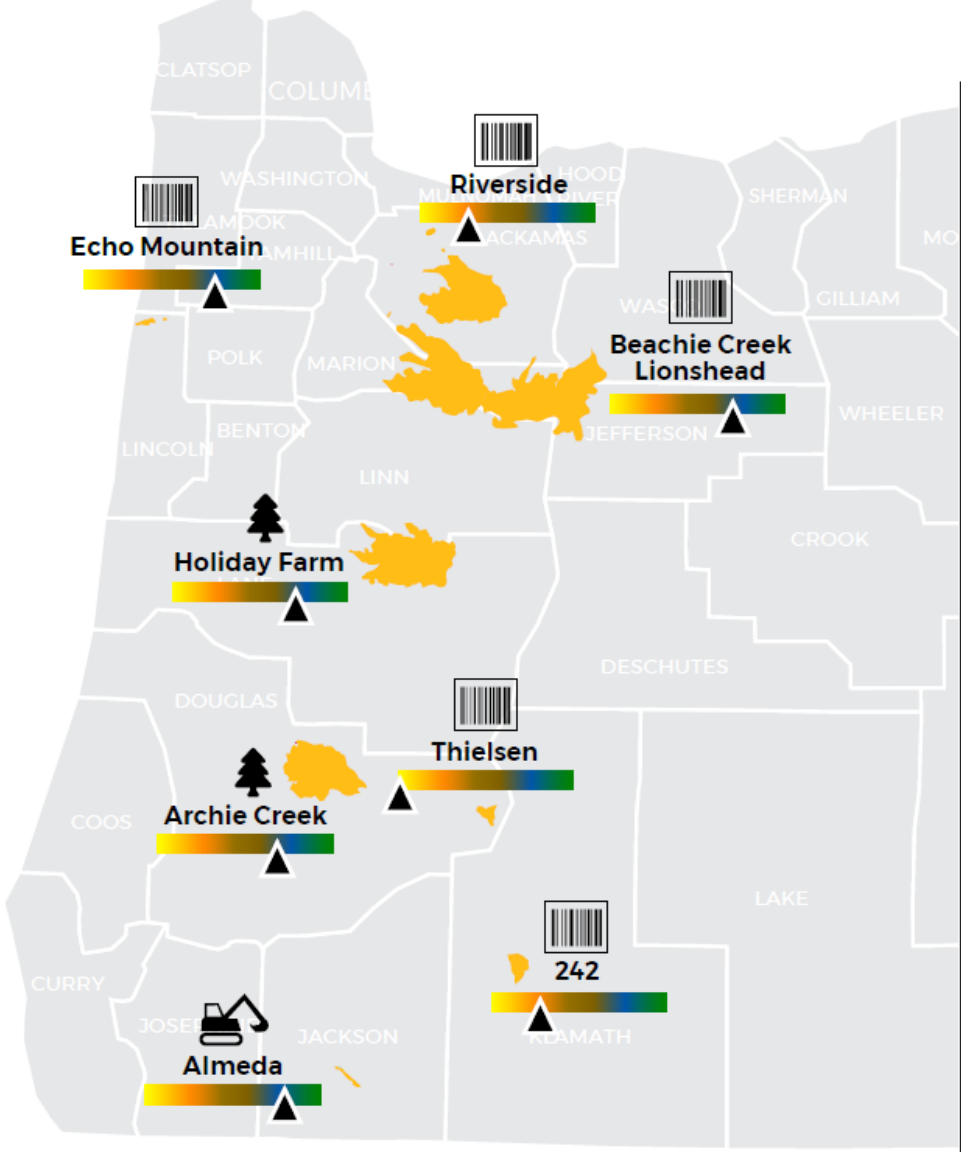


**472 home sites cleaned** throughout Oregon

**1,532 properties** currently participating in the Step 2 cleanup process



**42,007 trees marked** and ready to be cut



**10,201 hazard trees removed**



# BY THE NUMBERS

As of Friday 3/12/21


- **1,532 properties (2,986 home sites) participating** through complete Right of Entry forms (this number, and total number of home sites, will fluctuate)
- **56 monitoring crews and 67 contract crews** throughout Oregon
- **Contract crews will increase to 82** total in the next two weeks

**Legend:**



-  Environmental Testing
-  Tree Marking
-  Tree Removal
-  Debris Cleanup
-  Complete

# Data dashboard by fire and interactive status map: <https://bit.ly/3bMyqBl>

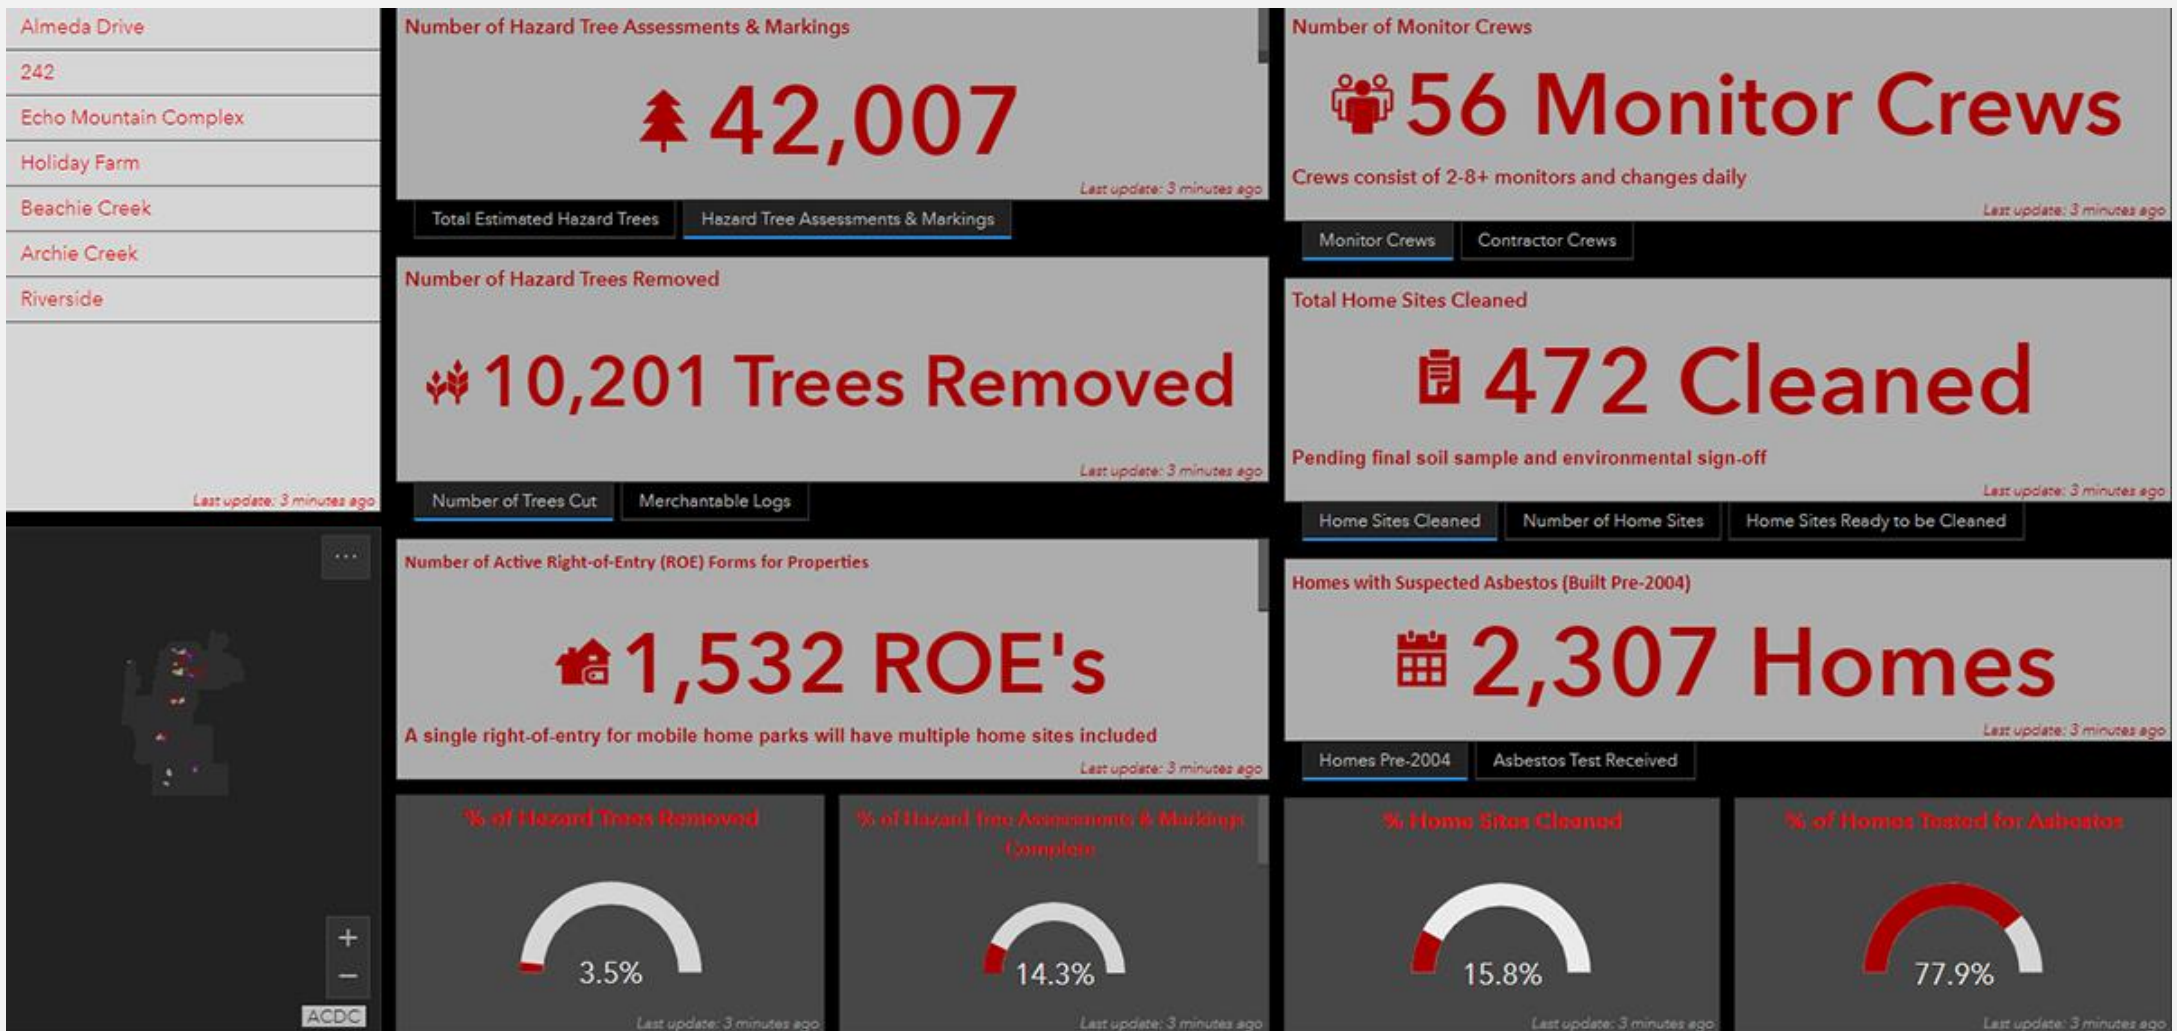

\*Data captured on Friday, March 12



# Private Property Debris Removal 3 week look ahead

Fire Area	Week 1 3/15-3/21	Week 2 3/22-3/28	Week 3 3/29-4/4	Total
<b>Alameda</b> <i>Ashbritt</i>	718 sites <u>ready for cleanup</u>	+ 76	+1,005	<b>1,799</b> out of <b>1,799</b> total sites
<b>Archie Creek</b> <i>K&amp;E Excavating</i>	28 sites <u>ready for cleanup</u>	+ 16	+ 31	<b>75</b> out of <b>75</b> total sites
<b>Beachie Creek</b> <i>ECC</i>	58 sites <u>ready for cleanup</u>	+ 33	+ 488	<b>579</b> out of <b>579</b> total sites
<b>Echo Mountain</b> <i>K&amp;E Excavating</i>	91 sites <u>ready for cleanup</u>	+14	+ 43	<b>148</b> out of <b>148</b> total sites
<b>Holiday Farm</b> <i>Ashbritt</i>	41 sites <u>ready for cleanup</u>	+45	+238	<b>324</b> out of <b>324</b> total sites
<b>Obenchain</b> <i>Not Assigned</i>	0 sites <u>ready for cleanup</u>	-	+ 16	<b>16</b> out of <b>16</b> total sites
<b>Riverside</b> <i>ECC</i>	12 sites <u>ready for cleanup</u>	+ 1	+ 20	<b>33</b> out of <b>33</b> total sites
<b>Two Four Two</b> <i>K&amp;E Excavating</i>	0 sites <u>ready for cleanup</u>	-	+ 12	<b>12</b> out of <b>12</b> total sites
				<b>Total = 2,986 out of 2,986 total sites ready</b>

# Hazard Tree Removal 3 week look ahead

Fire Area	Week 1 3/15-3/21	Week 2 3/22-3/28	Week 3 3/29-4/4	Total
<b>Almeda</b> <i>Ashbritt</i>	2,263 trees <u>ready for removal</u>	+ 50	+162	<b>2,475</b> out of <b>2,475</b> total trees
<b>Archie Creek</b> <i>Ceres Environmental</i>	11,462 trees <u>ready for removal</u>	+ 3,600	+ 3,600	<b>18,662</b> out of <b>49,000</b> total trees
<b>Beachie Creek</b> <i>ECC</i>	12,140 trees <u>ready for removal</u>	+ 3,600	+ 3,600	<b>19,340</b> out of <b>57,000</b> total trees
<b>Echo Mountain</b> <i>K&amp;E Excavating</i>	526 trees <u>ready for removal</u>	+ 20	+ 30	<b>576</b> out of <b>576</b> total trees
<b>Holiday Farm</b> <i>Suulutaaq</i>	16,300 trees <u>ready for removal</u>	+ 3,600	+3,600	<b>23,500</b> out of <b>70,000</b> total trees
<b>Riverside</b> <i>ECC</i>	12,313 trees <u>ready for removal</u>	+ 3,600	+ 3,600	<b>19,513</b> out of <b>113,000</b> total trees
<b>Two Four Two</b> <i>Ceres Environmental</i>	1,082 trees <u>ready for removal</u>	+ 50	+ 50	<b>1,182</b> out of <b>1,182</b> total trees

**Total = 85,248 out of 293,233 total trees ready**

# Track status with us



[Youtube.com/OregonDOT](https://www.youtube.com/OregonDOT)



[Twitter.com/OregonOEM](https://twitter.com/OregonOEM)



[Flickr.com/oregondot](https://www.flickr.com/oregondot)

Webpage, interactive status map, dashboard  
[wildfire.oregon.gov/cleanup](https://wildfire.oregon.gov/cleanup)

Debris news page  
[www.DebrisCleanupNews.com](http://www.DebrisCleanupNews.com)



[odot.wildfire@odot.state.or.us](mailto:odot.wildfire@odot.state.or.us)



**Hotline: 503-934-1700**
