



OREGON

Debris Management
Task Force

Wildfire Debris & Hazard Tree Removal Update

HOUSE SPECIAL COMMITTEE ON WILDFIRE RECOVERY




MARCH 22, 2021




Weekly topline points | from the week of March 15-19


- **157 cleared sites added this week for a total of 629 statewide** (out of 2,958 total home sites).
- Hazard tree marking and removal progressing: **52,455 trees marked and 10,971 removed** of the more than 290,000 estimated statewide.
- **Fire-impacted corridors continue to be extremely busy** with activity as many different jurisdictions share limited space. Spring Break travel will add to this. We ask everyone to use caution and expect delays.
- **Please submit a Right of Entry agreement soon to participate.** Submitting now helps crews keep a swift pace and accelerate to future sites. For those not participating, we ask everyone to be aware of the required steps involved.
- **Challenges to note:** planning for daily landfill capacity constraints, steep terrain for hazard tree marking, a phased process for removing debris

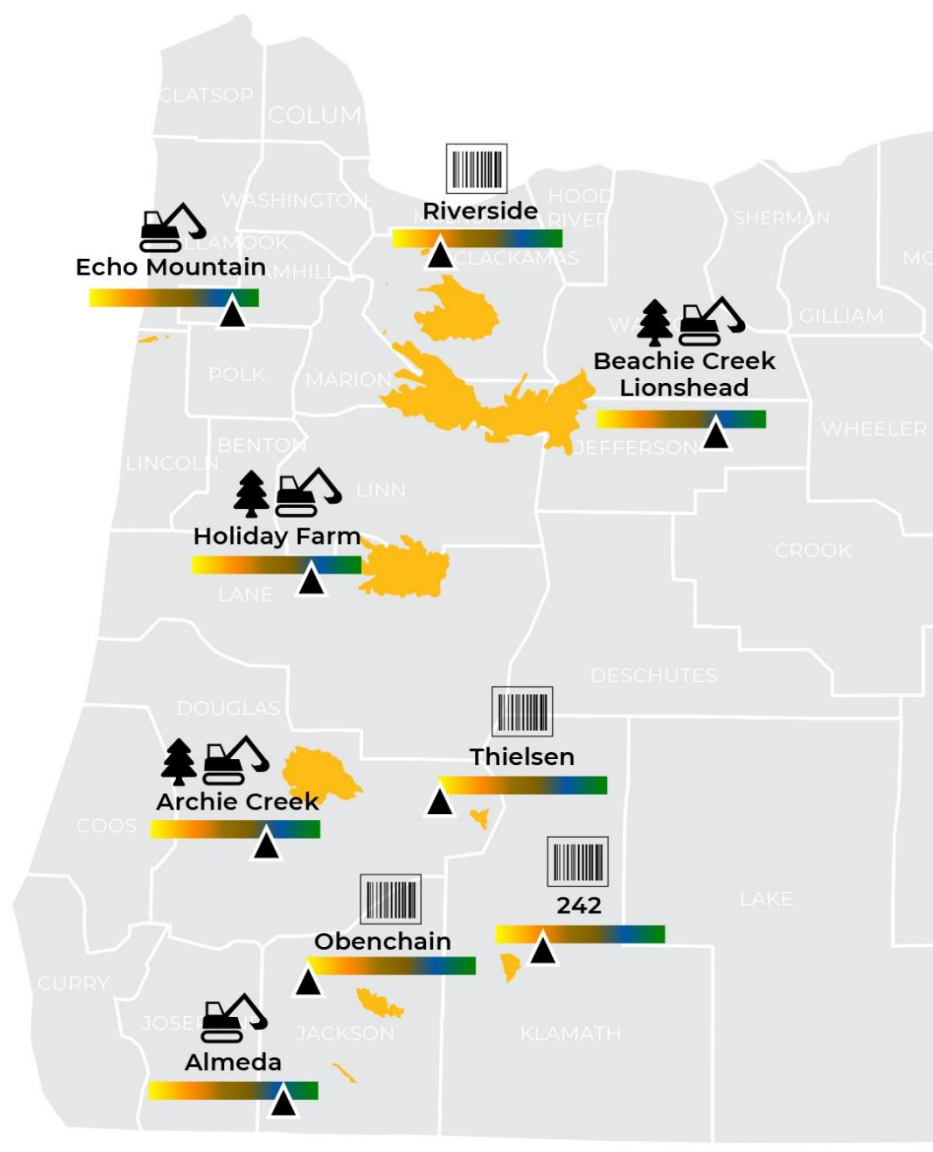

BY THE NUMBERS

As of Friday 3/19/21


665 home sites cleaned throughout Oregon

1,506 properties and 2,958 home sites currently participating in the Step 2 cleanup process 

52,419 trees marked and ready to be cut 


10,985 hazard trees removed 

- **1,506 properties and 2,958 home sites participating** through complete Right of Entry forms (this number fluctuates).
- **Number of crews working continues to increase: 77 contractor crews, 60 monitoring crews** currently working. Expecting contract crews to reach 82 in next week.

 Environmental Testing
  Tree Marking
  Tree Removal
  Debris Cleanup
  Complete




Data dashboard by fire and interactive status map <https://bit.ly/3bMyqBl>

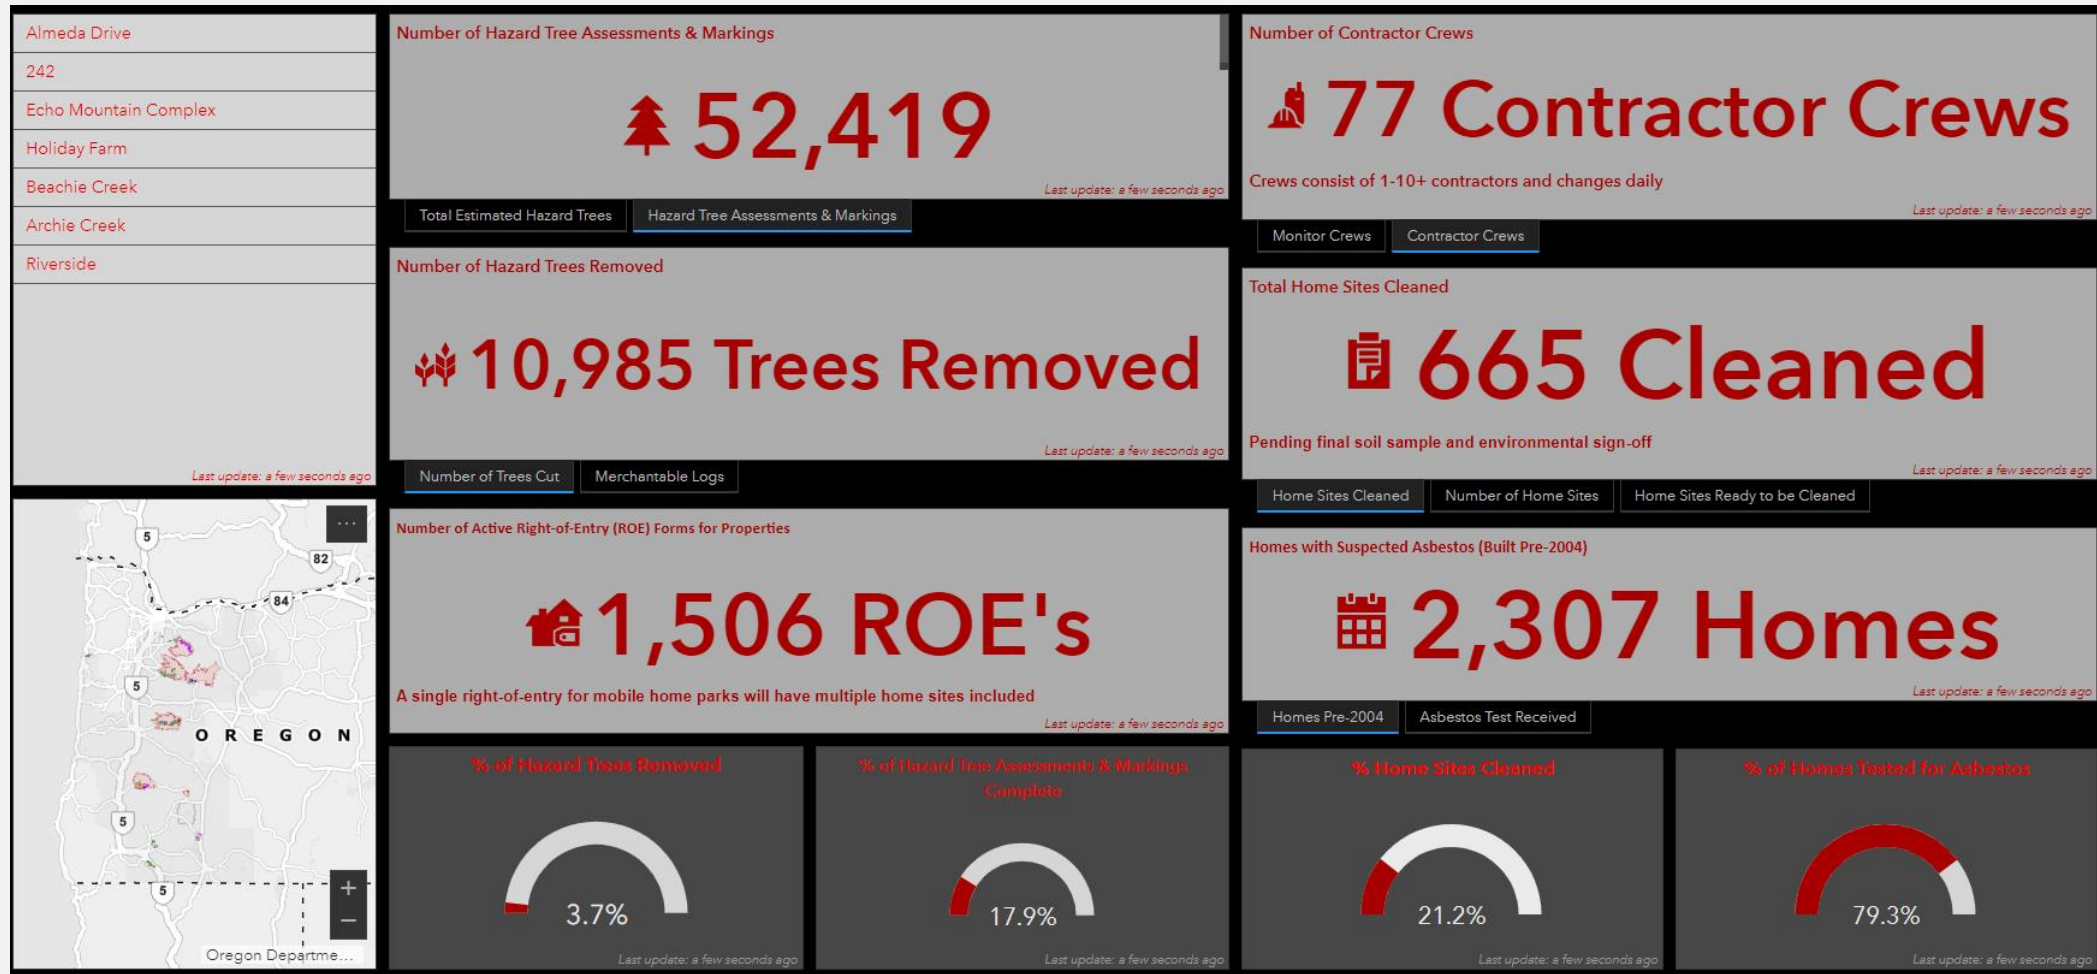

*Data captured on Friday, March 19

Hazard Tree Removal and Private Property Debris Removal look ahead: northern Oregon

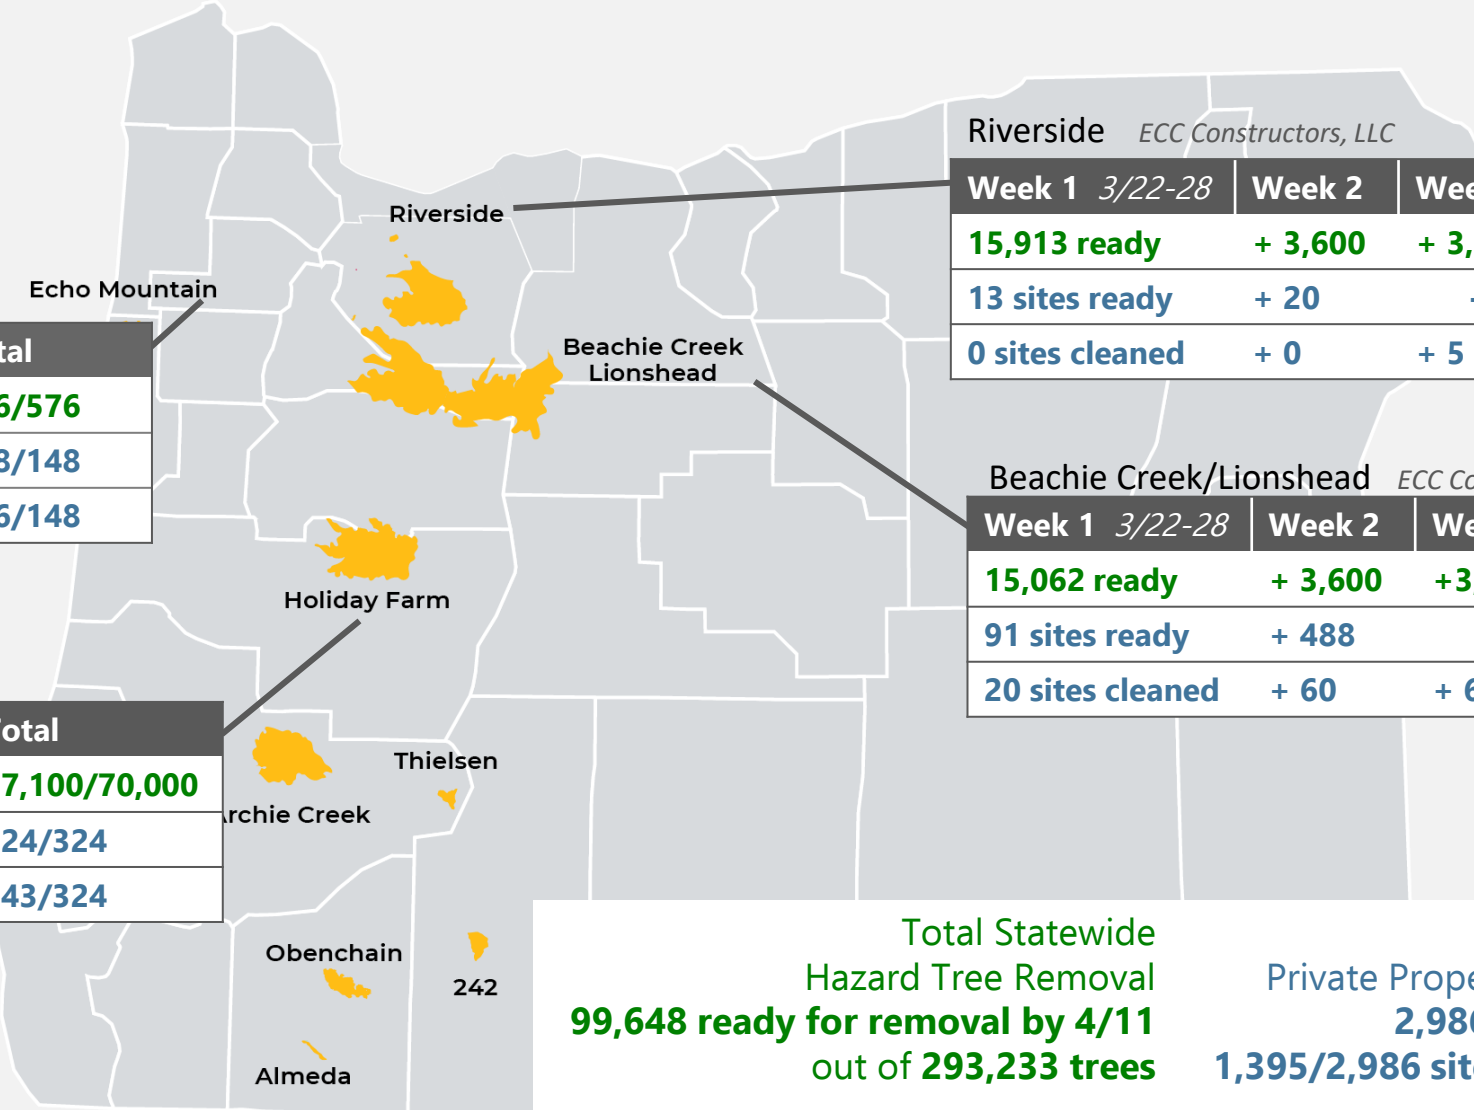

Echo Mountain *K&E Excavating, Inc.*

Week 1 3/22-28	Week 2	Week 3	Total
546 ready	+ 30	-	576/576
105 sites ready	+ 43	-	148/148
46 sites cleaned	+ 30	+ 30	106/148

Riverside *ECC Constructors, LLC*

Week 1 3/22-28	Week 2	Week 3	Total
15,913 ready	+ 3,600	+ 3,600	23,113/113,000
13 sites ready	+ 20	-	33/33
0 sites cleaned	+ 0	+ 5	5/33

Beachie Creek/Lionshead *ECC Constructors, LLC*

Week 1 3/22-28	Week 2	Week 3	Total
15,062 ready	+ 3,600	+ 3,600	22,940/57,000
91 sites ready	+ 488	-	579/579
20 sites cleaned	+ 60	+ 60	140/579

Holiday Farm *Suulutaaq, AshBritt Environmental*

Week 1 3/22-28	Week 2	Week 3	Total
19,900 ready	+ 3,600	+ 3,600	27,100/70,000
86 sites ready	+ 238	-	324/324
63 sites cleaned	+ 40	+ 40	143/324

Total Statewide Hazard Tree Removal 99,648 ready for removal by 4/11 out of 293,233 trees

Total Statewide Private Property Debris Removal 2,986/2,986 sites ready 1,395/2,986 sites cleaned by 4/11

Hazard Tree Removal and Private Property Debris Removal look ahead: southern Oregon

Archie Creek *Ceres Environmental, K&E Excavating, Inc.*


Week 1 3/22-28	Week 2	Week 3	Total
15,062 ready	+ 3,600	+ 3,600	22,262/49,000
44 sites ready	+ 31	-	75/75
8 sites cleaned	+ 15	+ 15	38/75

Obenchain *To be assigned shortly*

Week 1 3/22-28	Week 2	Week 3	Total
-	-	-	-
0 sites ready	+16	-	16/16
0 sites cleaned	+ 0	+ 5	5/16

Almeda *Ashbritt Environmental*

Week 1 3/22-28	Week 2	Week 3	Total
2,313 ready	+ 162	-	2,475/2,475
794 sites ready	+ 1,005	-	1,799/1,799
713 sites cleaned	+ 120	+ 120	953/1,799

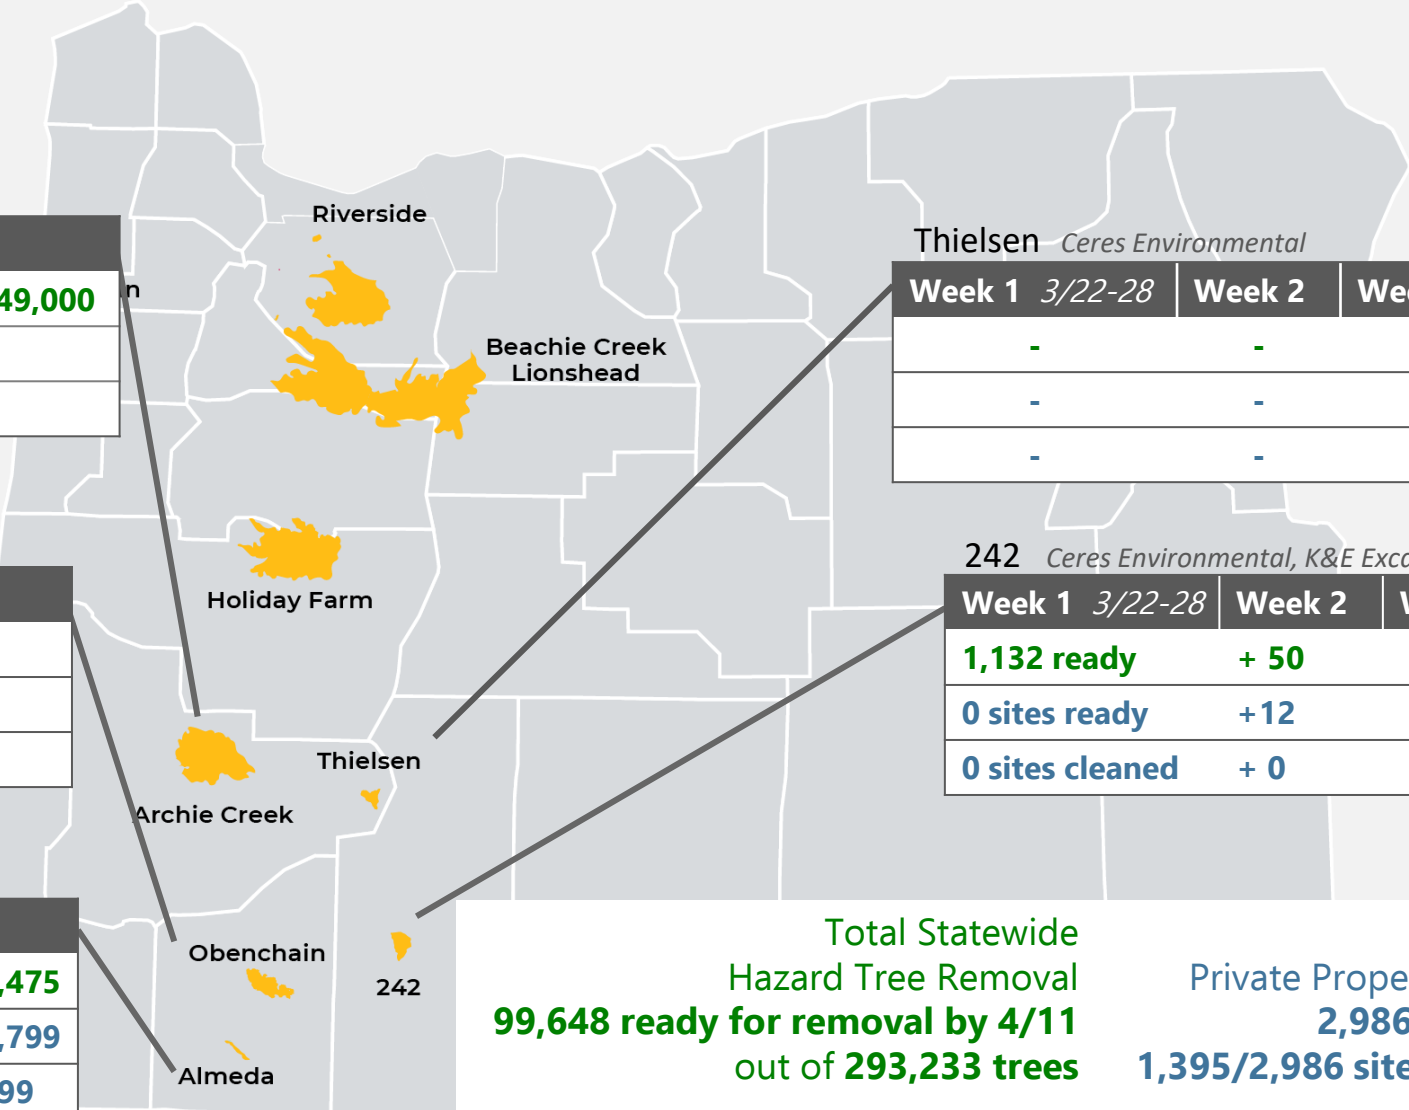

Thielsen *Ceres Environmental*

Week 1 3/22-28	Week 2	Week 3	Total
-	-	-	-
-	-	-	-
-	-	-	-

242 *Ceres Environmental, K&E Excavating, Inc.*

Week 1 3/22-28	Week 2	Week 3	Total
1,132 ready	+ 50	-	1,182/1,182
0 sites ready	+12	-	12/12
0 sites cleaned	+ 0	+ 5	5/12

Total Statewide Hazard Tree Removal 99,648 ready for removal by 4/11 out of 293,233 trees

Total Statewide Private Property Debris Removal 2,986/2,986 sites ready 1,395/2,986 sites cleaned by 4/11

Track status with us



[Youtube.com/OregonDOT](https://www.youtube.com/OregonDOT)



[Twitter.com/OregonOEM](https://twitter.com/OregonOEM)



[Flickr.com/oregondot](https://www.flickr.com/oregondot)

Webpage, interactive status map, dashboard
wildfire.oregon.gov/cleanup

Debris news page
www.DebrisCleanupNews.com



odot.wildfire@odot.state.or.us



Hotline: 503-934-1700
