



OREGON

Debris Management
Task Force

Wildfire Debris & Hazard Tree Removal Update

HOUSE SPECIAL COMMITTEE ON WILDFIRE RECOVERY




MARCH 29, 2021




Weekly topline points | from the week of March 22-26

- **260 cleared sites completed this week for a total of 889 statewide** (out of 2,868 total home sites).
- Hazard tree marking and removal steadily progressing: **57,694 trees marked and 18,401 removed** of the more than 290,000 estimated statewide.
- **Fire-impacted corridors continue to be extremely busy** with activity as many different jurisdictions share limited space. We ask everyone to use caution, expect delays, and practice safe driving in these areas.
- **We continue to find efficient ways to increase pace and progress.** Operational examples: on extremely steep slopes, we're using drone technology to identify and mark hazard trees, and using on-site metal recycling to save on hauling time and capacity.

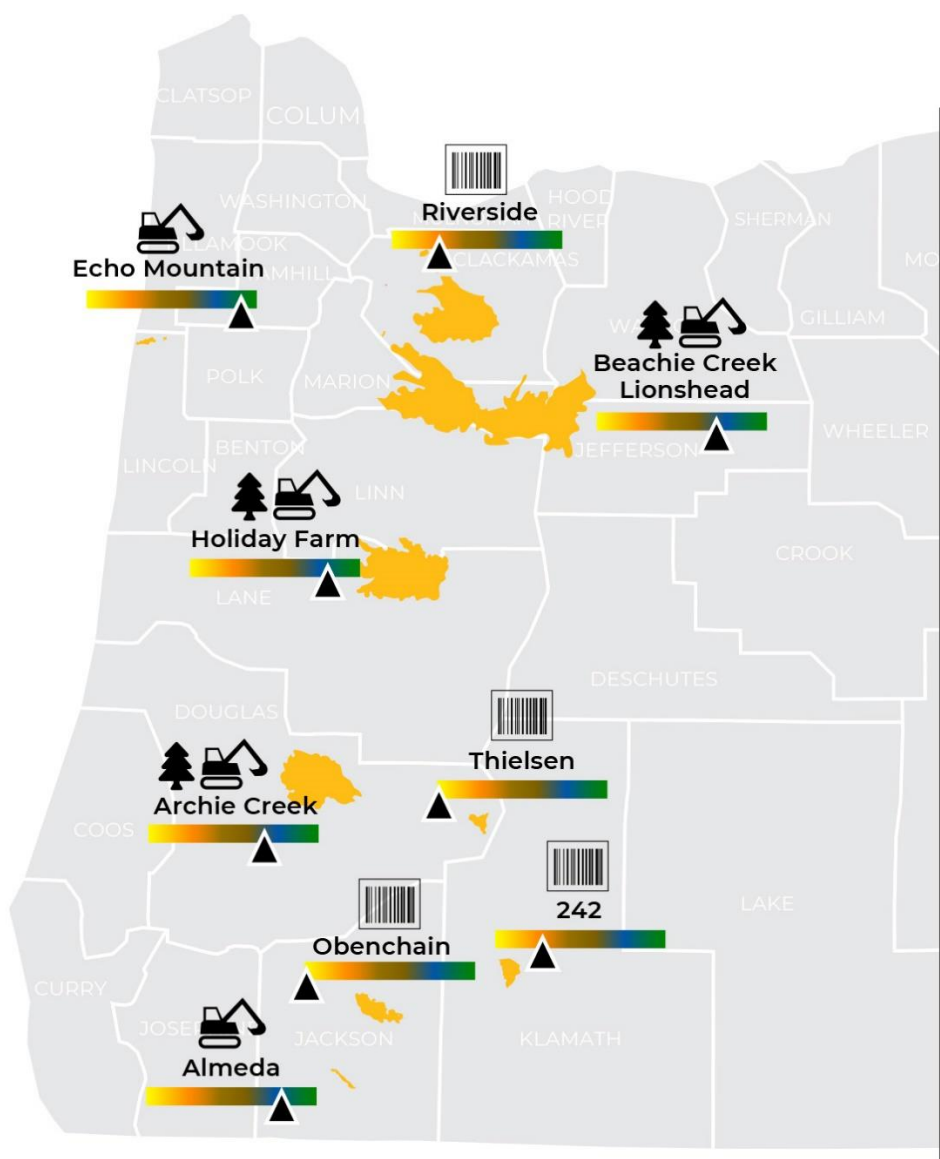


BY THE NUMBERS

As of Friday 3/26/21



889 home sites cleaned throughout Oregon

1,488 properties and 2,868 home sites currently participating in the Step 2 cleanup process



57,694 trees marked and ready to be cut




18,401 hazard trees removed




- **1,488 properties and 2,868 home sites participating** through complete Right of Entry forms (this number fluctuates).
- **Number of crews working continues to increase: 82 contractor crews, 55 monitoring crews** currently working.

Data dashboard by fire and interactive status map <https://bit.ly/3bMyqBl>

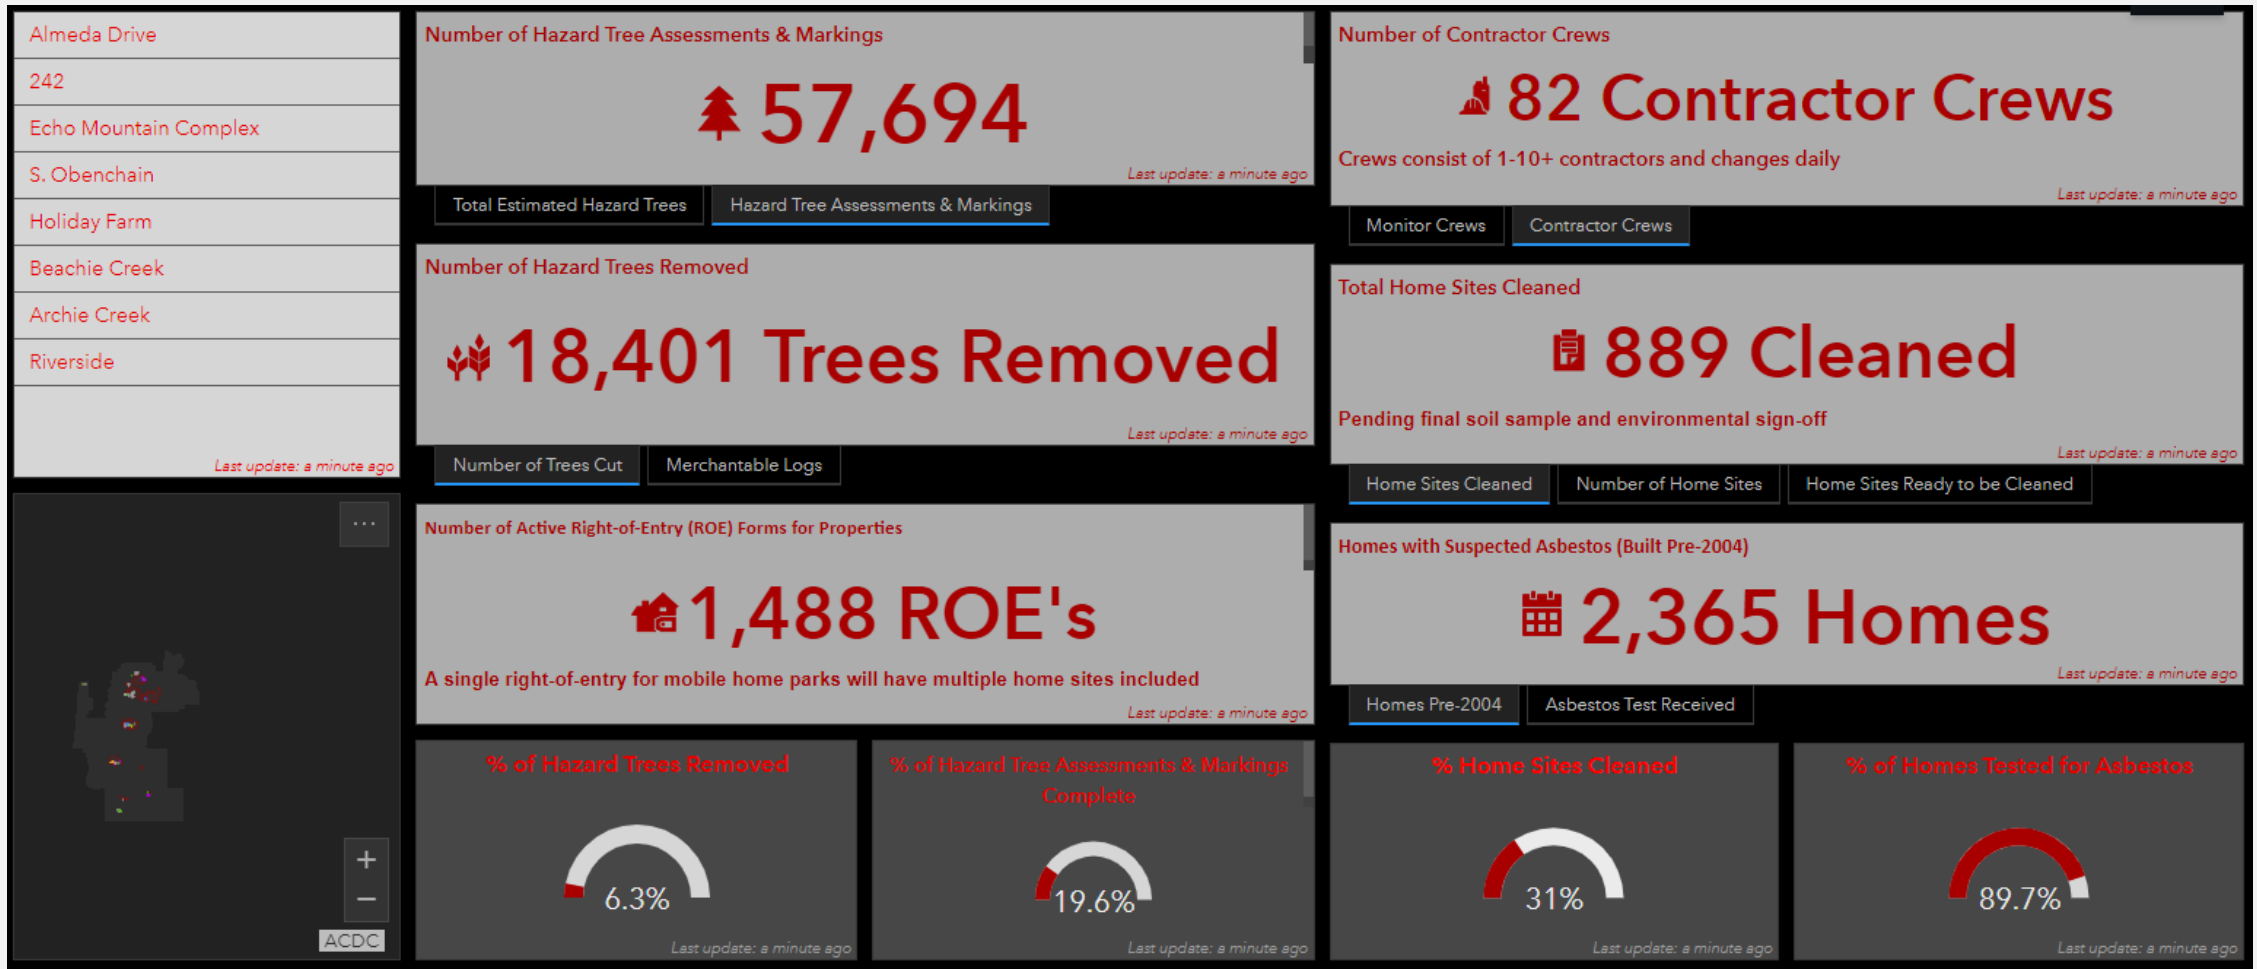

*Data captured on Friday, March 26

Hazard Tree Removal and Private Property Debris Removal look ahead: northern Oregon

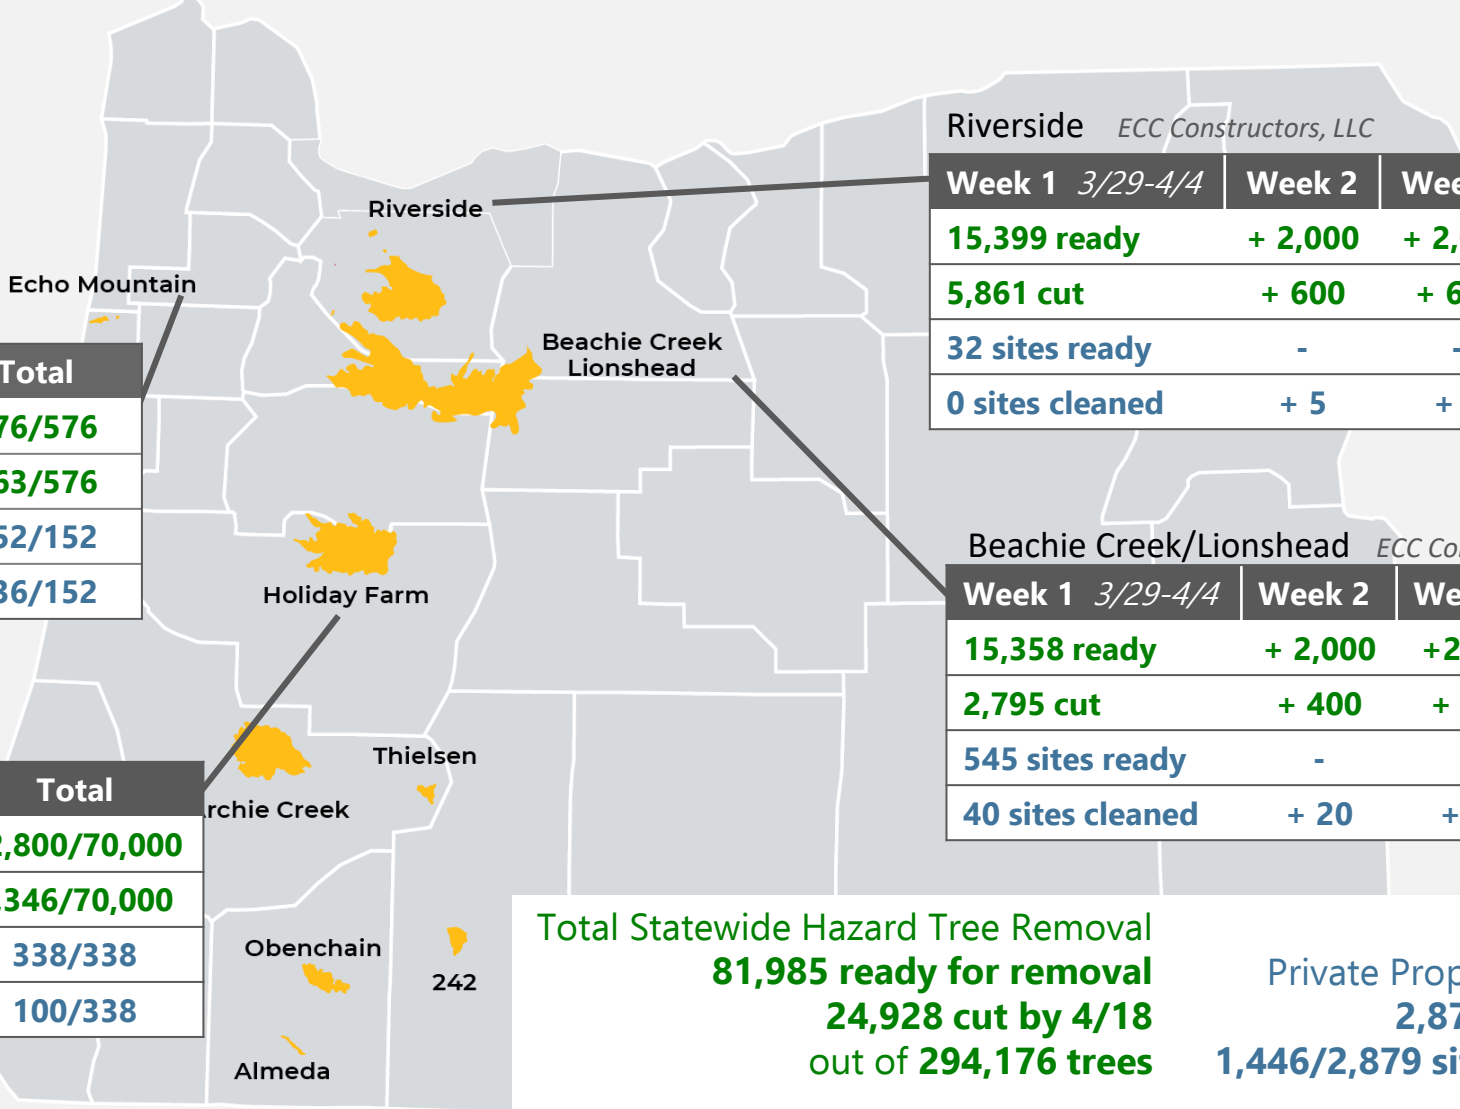

Echo Mountain *K&E Excavating, Inc.*

Week 1 3/29-4/4	Week 2	Week 3	Total
576 ready	-	-	576/576
243 cut	+ 10	+ 10	263/576
152 sites ready	-	-	152/152
76 sites cleaned	+ 30	+ 30	136/152

Holiday Farm *Suulutaaq, AshBritt Environmental*

Week 1 3/29-4/4	Week 2	Week 3	Total
18,800 ready	+ 2,000	+ 2,000	22,800/70,000
8,346 cut	+ 500	+ 500	9,346/70,000
338 sites ready	-	-	338/338
60 sites cleaned	+ 20	+ 20	100/338

Riverside *ECC Constructors, LLC*

Week 1 3/29-4/4	Week 2	Week 3	Total
15,399 ready	+ 2,000	+ 2,000	19,399/113,000
5,861 cut	+ 600	+ 600	7,061/113,000
32 sites ready	-	-	32/32
0 sites cleaned	+ 5	+ 5	10/32

Beachie Creek/Lionshead *ECC Constructors, LLC*

Week 1 3/29-4/4	Week 2	Week 3	Total
15,358 ready	+ 2,000	+ 2,000	19,358/57,000
2,795 cut	+ 400	+ 400	3,995/57,000
545 sites ready	-	-	545/545
40 sites cleaned	+ 20	+ 20	80/545

Total Statewide Hazard Tree Removal
81,985 ready for removal
24,928 cut by 4/18
 out of **294,176 trees**

Total Statewide Private Property Debris Removal
2,879/2,879 sites ready
1,446/2,879 sites cleaned by 4/18

Hazard Tree Removal and Private Property Debris Removal look ahead: southern Oregon

Archie Creek *Ceres Environmental, K&E Excavating, Inc.*

Week 1 3/29-4/4	Week 2	Week 3	Total
11,252 ready	+ 2,000	+ 2,000	15,252/49,000
2,863 cut	+ 600	+ 600	4,063/49,000
76 sites ready	-	-	76/76
11 sites cleaned	+ 8	+ 8	27/76

Obenchain *To be assigned shortly*

Week 1 3/29-4/4	Week 2	Week 3	Total
-	-	-	-
-	-	-	-
17 sites ready	-	-	17/17
0 sites cleaned	+ 5	+ 5	10/17

Alameda *Ashbritt Environmental*


Week 1 3/29-4/4	Week 2	Week 3	Total
2,650 ready	+ 100	-	2,750/2,750
0 cut	-	+ 100	100/2,750
1,707 sites ready	-	-	1,707/1,707
833 sites cleaned	+ 120	+ 120	1,073/1,707

Thielsen *Ceres Environmental*

Week 1 3/29-4/4	Week 2	Week 3	Total
-	-	-	-
-	-	-	-
-	-	-	-
-	-	-	-

242 *Ceres Environmental, K&E Excavating, Inc.*

Week 1 3/29-4/4	Week 2	Week 3	Total
1,850 ready	-	-	1,850/1,850
0 cut	0	+ 100	100/1,850
12 sites ready	-	-	12/12
0 sites cleaned	+ 5	+ 5	10/12

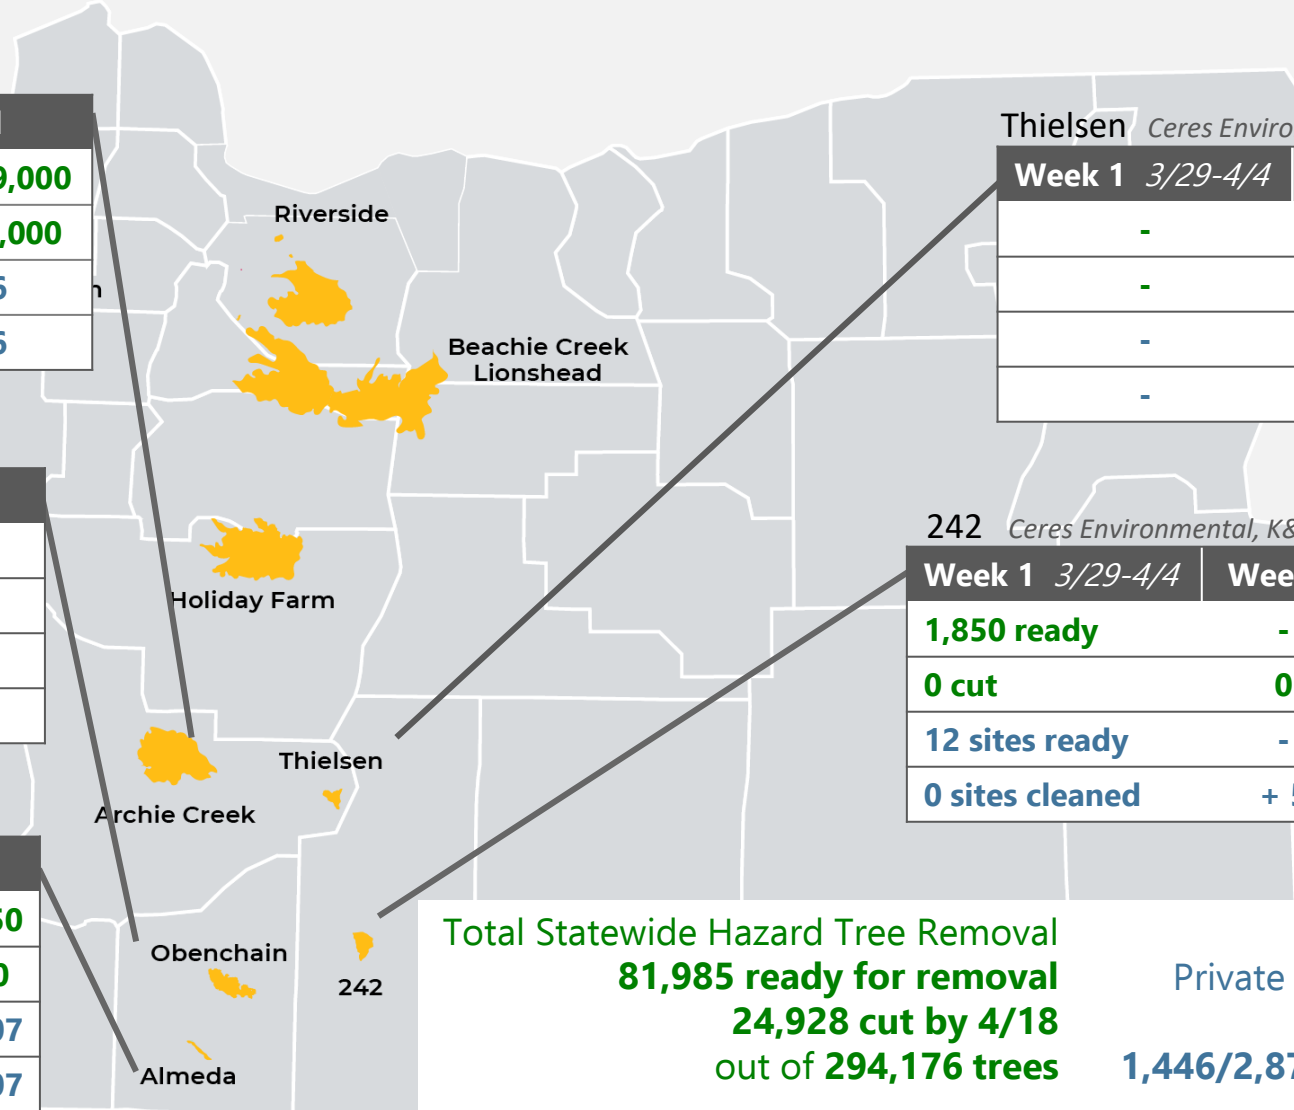

Total Statewide Hazard Tree Removal
81,985 ready for removal
24,928 cut by 4/18
 out of **294,176 trees**

Total Statewide Private Property Debris Removal
2,879/2,879 sites ready
1,446/2,879 sites cleaned by 4/18

Track status with us



Youtube.com/[OregonDOT](https://www.youtube.com/OregonDOT)



Twitter.com/[OregonOEM](https://twitter.com/OregonOEM)



Flickr.com/[oregondot](https://www.flickr.com/oregondot)

Webpage, interactive status map, dashboard
wildfire.oregon.gov/cleanup

Debris news page
www.DebrisCleanupNews.com



odot.wildfire@odot.state.or.us



Hotline: 503-934-1700
